

GENERAL NOTES

- CONSTRUCTION TRAFFIC SHALL YIELD TO AIRCRAFT TRAFFIC AT ALL TIMES.
 - BARRICADE PLACEMENT AND PAVEMENT MARKING OBLITERATION MAY BE ADJUSTED AT THE DISCRETION OF THE CITY AND/OR AIRPORT STAFF TO ACCOMMODATE SPECIFIC AIRCRAFT MOVEMENT NEEDS.
 - MAINTAIN ACCESS TO THE EXISTING TERMINAL AT ALL TIMES.
 - ANTICIPATED CONSTRUCTION TIMEFRAME (IF AWARDED):
- CONSTRUCTION NTP: AUG 1ST, 2020
- BASE BID**
- PHASE 1: AUG 3-31, 2020
PHASE 2: SEP 1-29, 2020
PHASE 3: SEP 30-NOV 14, 2020
WINTER BREAK: NOV 15, 2020-FEB 28, 2021
- ADD-ALT NO.1**
- PHASE 4: MAR 1-MAY 30, 2021
PHASE 5: MAY 31-JUL 30, 2021
PHASE 6: JUL 31-SEP 29, 2021

LEGEND - BASE BID


	PHASE 1A	(28 CAL. DAYS)
	PHASE 1B	(7 CAL. DAYS, CONCURRENT W/ PH. 1A)
	PHASE 1C	(65 CAL. DAYS, CONCURRENT W/ PHS. 1-3)
	PHASE 2A	(28 CAL. DAYS)
	PHASE 2B	(3 NIGHTS, CONCURRENT W/ PH. 2A)
	PHASE 3A	(45 CAL. DAYS)
	PHASE 3B	(10 NIGHTS, CONCURRENT W/ PH. 3A)

LEGEND - ADD ALT NO.1

	PHASE 4A	(90 CAL. DAYS)
	PHASE 4B	(7 NIGHTS, CONCURRENT W/ PH. 4A)
	PHASE 4C	(21 CAL. DAYS, CONCURRENT W/ PH. 4A)
	PHASE 4D	(28 CAL. DAYS, CONCURRENT W/ PH. 4A)
	PHASE 5A	(60 CAL. DAYS)
	PHASE 5B	(28 NIGHTS, CONCURRENT W/ PH. 5A)
	PHASE 5C	(21 CAL. DAYS, CONCURRENT W/ PH. 5A)
	PHASE 6A	(60 CAL. DAYS)
	PHASE 6B	(28 NIGHTS, CONCURRENT W/ PH. 6A)
	PHASE 6C	(21 CAL. DAYS, CONCURRENT W/ PH. 6A)

GENERAL PHASING NOTES

- PHASES 4B & 4D SHALL NOT OCCUR CONCURRENTLY.
- PHASES MUST BE CONSTRUCTED IN CHRONOLOGICAL ORDER.
- ALL LOW-PROFILE BARRICADES SHALL BE PLACED AT THE RESPECTIVE RSA BOUNDARY OR TOFA BOUNDARY, WHICHEVER GOVERNS.
- CONTRACTOR SHALL PROVIDE & MAINTAIN ONE SET OF LIGHTED X'S DURING THIS PROJECT. THE AIRPORT WILL PROVIDE A SECONDARY SET WHEN TWO RUNWAYS ARE CLOSED AT THE SAME TIME. BOTH SETS SHALL BE MAINTAINED BY THE CONTRACTOR WHEN USED.
- THERE WILL BE A WINTER BREAK IN CONSTRUCTION BETWEEN PHASE 3 AND PHASE 4 (IF ADD-ALT NO.1 IS AWARDED.)
- BLACK PAINT WILL BE USED TO COVER UP TAXIWAY CENTERLINES AND/OR LEAD-IN LINES TEMPORARILY. THIS EFFORT WILL BE COORDINATED WITH AIRPORT BEFORE THE START OF EACH PHASE. THE WORK AND MATERIALS REQUIRED FOR THIS ITEM SHALL BE CONSIDERED INCIDENTAL TO THE OVERALL PROJECT (NPI).

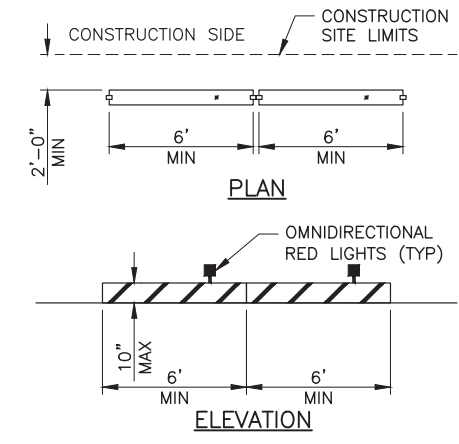

- NOTES:**
- LOW PROFILE BARRICADES AND LIGHTS SHALL BE PROVIDED AND MAINTAINED (DAY AND NIGHT) BY THE CONTRACTOR (NPI).
 - THE OWNER MAY DIRECT THE CONTRACTOR TO RELOCATE ANY BARRICADES AT THEIR DISCRETION.

1 LOW PROFILE BARRICADES NTS

REVISION	BY	DATE
CITY OF PRESCOTT PRESCOTT REGIONAL AIRPORT		
PRC PROJECT NO 19607		DIBBLE PROJECT NO 1018102.05
TAXIWAY C RELOCATION		
OVERALL PHASING PLAN		
DRN: TW/MS	DES: TCW	CK: MJB
DATE: 03/12/20	DATE: 03/12/20	DATE: 03/12/20
SCALE: 1" = 400'	G2.0	10 of 164



K:\2018\1018102.05_PRC_TW_C_RELOCATION\CAD\18102_05-02_X.DWG Mar. 25, 2020 5:13 PM
